



---

# Solar Probe Plus (SPP) Investigations AO Pre-Proposal Conference

## Living With A Star (LWS) Program Schedule

**John Lee**  
**Solar Probe Plus Program Executive**

**Science Mission Directorate**  
**NASA Headquarters**

**January 7, 2010**



# Solar Probe Plus Mission Schedule


---

**Table 4. Schedule for Solar Probe Plus Mission**

	<b>AO Date</b>	<b>New Date</b>
Start Phase A (KDP-A)	12/2009	
Start Phase B (KDP-B)	04/2012	07/2011
Preliminary Design Review (PDR)/ Non-Advocate Review (NAR)	01/2014	
Start Phase C (KDP-C / Confirmation)	07/2014	
Critical Design Review (CDR)	11/2015	
Flight Instrument delivery	08/2016	
Observatory Integration and Test	08/2016	
Launch	08/2018	
Start Phase E (KDP-E)	09/2018	
Start Phase F (KDP-F)	09/2025	



# Solar Probe Plus Mission Management

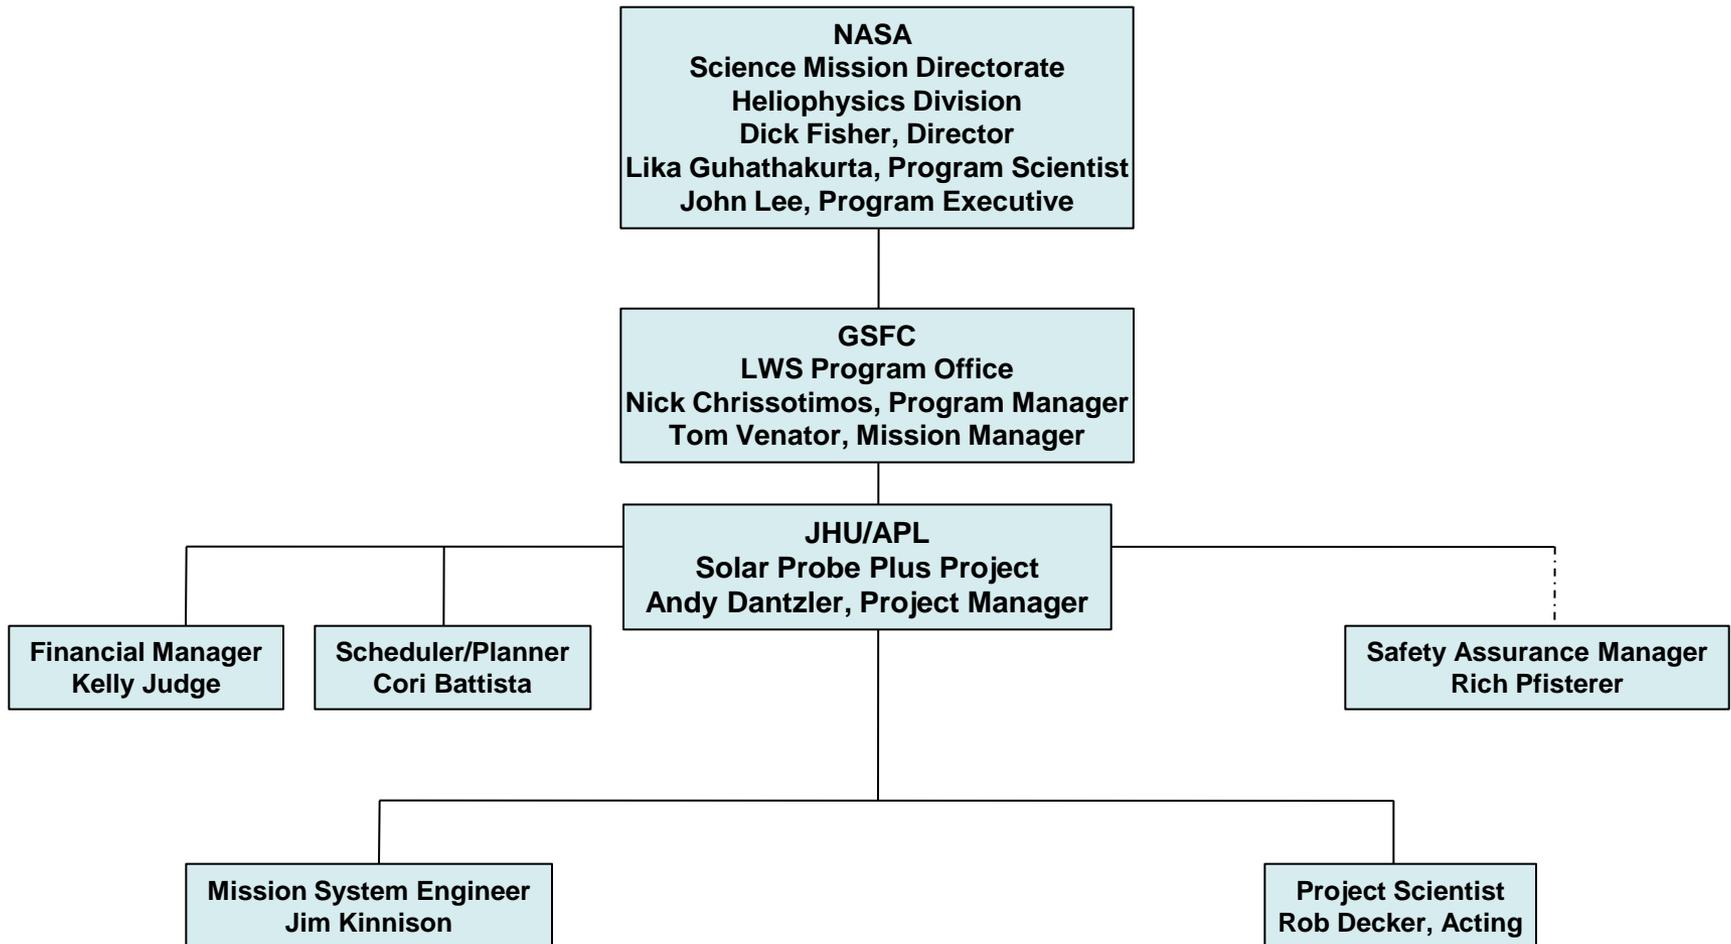



# Solar Probe Plus Mission Management

---

The NASA Interim Directive (NID) for NASA Procedural Requirements (NPR) 7120.5D is the governing NASA Procedural Requirements

- LWS Program Manager resides at GSFC and reports administratively to Center Director and Center Management Council, but functionally to SMD Heliophysics Division Director
- SPP Project and the Project Manager resides at JHU/APL and reports to LWS Program Manager
- SPP Instruments management will reside at JHU/APL
